PLANT DRAIN PUMP STATION
FILTER BUILDING
UV BUILDING
HEADWORKS BUILDING
FLAMMABLES STORAGE BUILDING
PRIMARY CLARIFIER #1
PRIMARY CLARIFIER #2
PC SPLITTER
FINAL CLARIFIER #3
FERRIC
ODOR CONTROL #2
DAF BASIN #1
FINAL CLARIFIER #2
DAF BASIN #2
SLUDGE BUILDING
FC SPLITTER
CARBON
FINAL CLARIFIER #1
DEWATERING
ODOR CONTROL #1
BNR BASIN #3
BNR BASIN #2
SWITCHGEAR
CENTRATE
BNR BASIN #1
BNR SPLITTER
BASIN BLOWER BUILDING
NALL AVENUE
BERMS & LANDSCAPING
DIGESTER #1
DIGESTER #2
DIGESTER CONTROL BUILDING
DIGESTER #3
CEPT
LINE REPAIR ADMIN
TC-12
ROAD E
GAS FLARE
SWITCHGEAR
FS SERIES 815
TC-11 / LINE MAINTENANCE
ADMIN STORAGE
ADMIN BLDG
BERMS & LANDSCAPING
49TH STREET

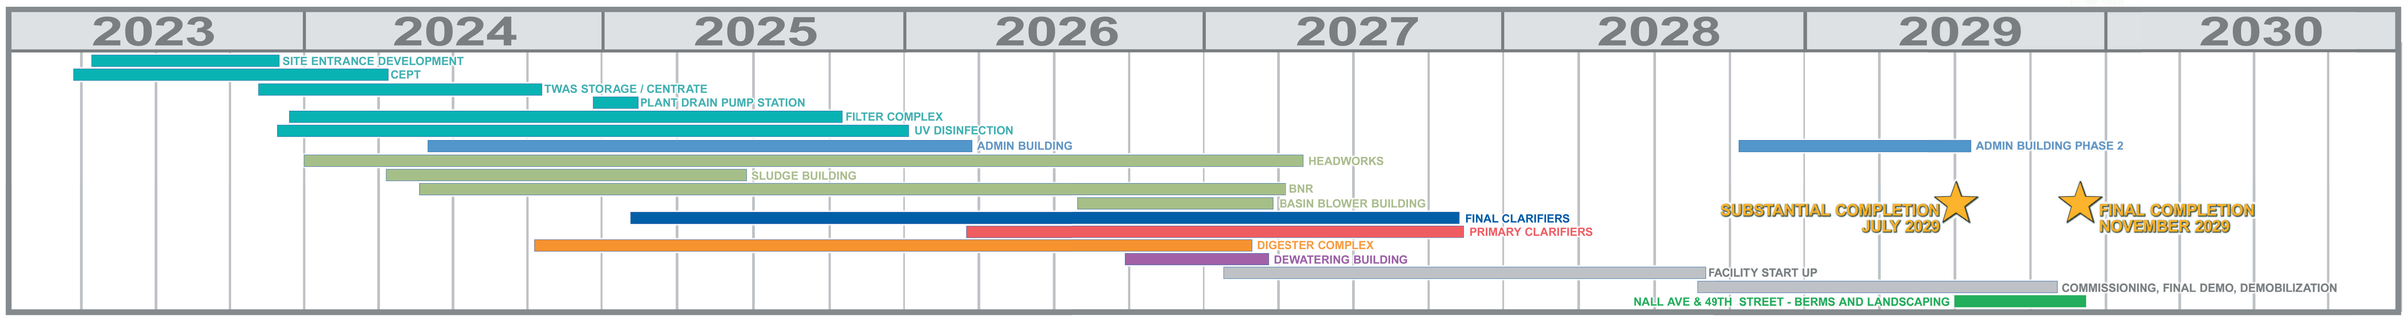
2023
2024
2025
2026
2027
2028
2029
2030
SITE ENTRANCE DEVELOPMENT
CEPT
TWAS STORAGE / CENTRATE
PLANT DRAIN PUMP STATION
FILTER COMPLEX
UV DISINFECTION
ADMIN BUILDING
HEADWORKS
SLUDGE BUILDING
BNR
BASIN BLOWER BUILDING
FINAL CLARIFIERS
PRIMARY CLARIFIERS
DIGESTER COMPLEX
DEWATERING BUILDING
FACILITY START UP
NALL AVE & 49TH STREET - BERMS AND LANDSCAPING
ADMIN BUILDING PHASE 2
SUBSTANTIAL COMPLETION JULY 2029
FINAL COMPLETION NOVEMBER 2029
COMMISSIONING, FINAL DEMO, DEMOBILIZATION
